

Project Planning Phase

Project Planning Template (Product Backlog, Sprint Planning, Stories, Story Points)

Date: 31 July 2026

Team ID: _____

Project Name: ServiceNow-Based Employee Laptop Request Application

Maximum Marks: 5 Marks

Product Backlog, Sprint Schedule, and Estimation (4 Marks)

Use the below template to create product backlog and sprint schedule.

Sprint	Functional Requirement (Epic)	User Story No.	User Story / Task	Story Points	Priority	Team Members
Sprint-1	Authentication & Onboarding	USN-1	As an employee, I can log into the ServiceNow portal using my company SSO credentials.	3	High	Frontend, Backend
Sprint-1		USN-2	As an employee, I will receive a confirmation email once I have logged in for the first time.	2	Medium	Backend
Sprint-1		USN-3	As an employee/manager/IT agent, I can view a role-based dashboard relevant to my access level.	3	High	Frontend
Sprint-1	Laptop Request Catalog	USN-4	As an employee, I can browse the Laptop Request catalog item to view available laptop models.	2	High	ServiceNow Dev
Sprint-1		USN-5	As an employee, I can submit a laptop request by filling out model, justification, and urgency.	5	High	ServiceNow Dev
Sprint-1		USN-6	As an employee, I can attach supporting documents (e.g. manager memo) to my laptop request.	5	Medium	ServiceNow Dev
Sprint-2	Approval Workflow	USN-7	As a manager, I can view pending laptop requests from my team and approve or reject them.	5	High	Workflow Dev
Sprint-2		USN-8	As an IT approver, I can review approved requests and verify asset availability before final approval.	5	High	Workflow Dev
Sprint-2		USN-9	As an employee, I will receive email notifications at each approval stage of my request.	3	Medium	Backend
Sprint-2		USN-10	As a manager/IT approver, I can reject a request with a mandatory reason comment.	2	Medium	Workflow Dev
Sprint-2		USN-11	As an admin, the system escalates a pending approval to the next approver after an SLA breach.	5	Low	Workflow Dev
Sprint-3	Fulfillment & Asset Tracking	USN-12	As an IT agent, I can assign a laptop asset to an approved request.	5	High	Asset Mgmt Dev
Sprint-3		USN-13	As an IT agent, I can update the request status (In Fulfillment / Shipped / Delivered).	3	High	Asset Mgmt Dev
Sprint-3		USN-14	As an employee, I can track the real-time status of my laptop request from the portal.	3	Medium	Frontend
Sprint-3		USN-15	As an IT agent, I can update asset inventory once a laptop is issued.	5	Medium	Asset Mgmt Dev
Sprint-3		USN-16	As an employee, I can confirm receipt of my laptop, closing the request.	4	High	Frontend
Sprint-4	Reporting & Admin	USN-17	As an admin, I can generate a report on laptop request volume by department.	5	Medium	Reporting Dev

Sprint	Functional Requirement (Epic)	User Story No.	User Story / Task	Story Points	Priority	Team Members
Sprint-4		USN-18	As an admin, I can generate a report on average request turnaround time.	5	Medium	Reporting Dev
Sprint-4		USN-19	As an admin, I can configure the approval matrix and SLA thresholds.	5	High	Workflow Dev
Sprint-4		USN-20	As an admin, I can view an audit log of all actions taken on a request.	5	Low	Reporting Dev

Project Tracker, Velocity & Burndown Chart (4 Marks)

Sprint	Total Story Points	Duration	Sprint Start Date	Sprint End Date (Planned)	Story Points Completed	Sprint Release Date (Actual)
Sprint-1	20	6 Days	03 Aug 2026	08 Aug 2026	20	08 Aug 2026
Sprint-2	20	6 Days	10 Aug 2026	15 Aug 2026		
Sprint-3	20	6 Days	17 Aug 2026	22 Aug 2026		
Sprint-4	20	6 Days	24 Aug 2026	29 Aug 2026		

Velocity

Sprint-1 ran for a 6-day duration and the team completed all 20 planned Story Points, so the team's velocity for Sprint-1 is 20 Story Points per Sprint. Let's calculate the team's average velocity (AV) per iteration unit (Story Points per day):

$$AV = \text{Velocity} / \text{Sprint Duration} = 20 / 6 \approx 3.33 \text{ Story Points per Day}$$

Burndown Chart

A burndown chart is a graphical representation of work remaining versus time, commonly used in Agile/Scrum methodologies to track a sprint's progress against the ideal completion pace. The chart below tracks Sprint-1 of the ServiceNow-Based Employee Laptop Request Application, where the team started with 20 Story Points and closed the sprint at zero remaining points by Day 6.

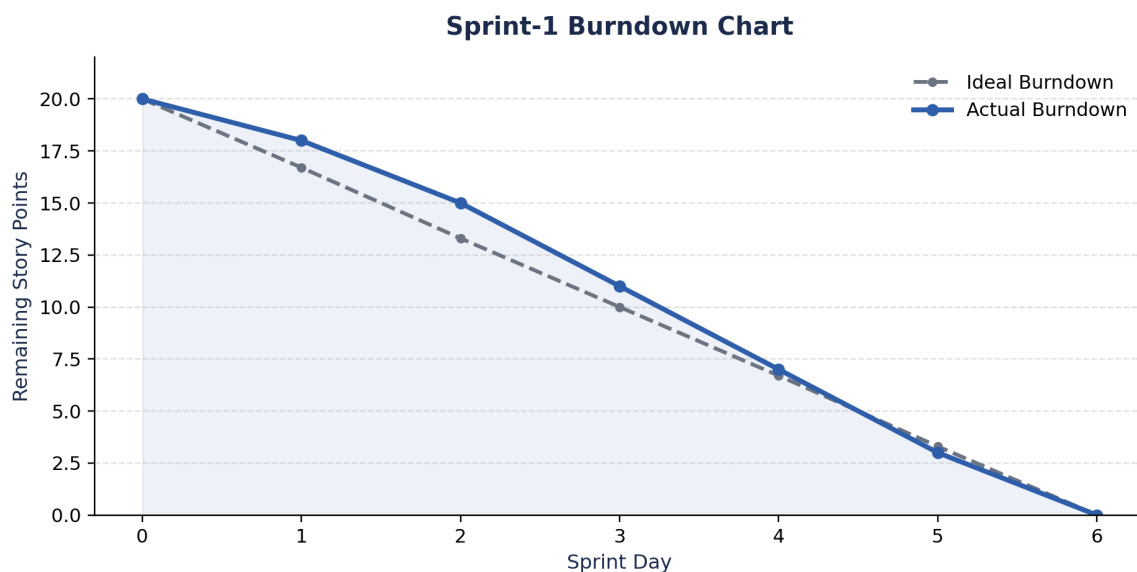


Figure: Sprint-1 ideal vs. actual burndown for the ServiceNow-Based Employee Laptop Request Application.

Reference

<https://www.atlassian.com/agile/project-management>
<https://www.atlassian.com/agile/tutorials/how-to-do-scrum-with-jira-software>
<https://www.atlassian.com/agile/tutorials/epics>
<https://www.atlassian.com/agile/tutorials/sprints>
<https://www.atlassian.com/agile/project-management/estimation>
<https://www.atlassian.com/agile/tutorials/burndown-charts>

<https://www.visual-paradigm.com/scrum/scrum-burndown-chart/>
